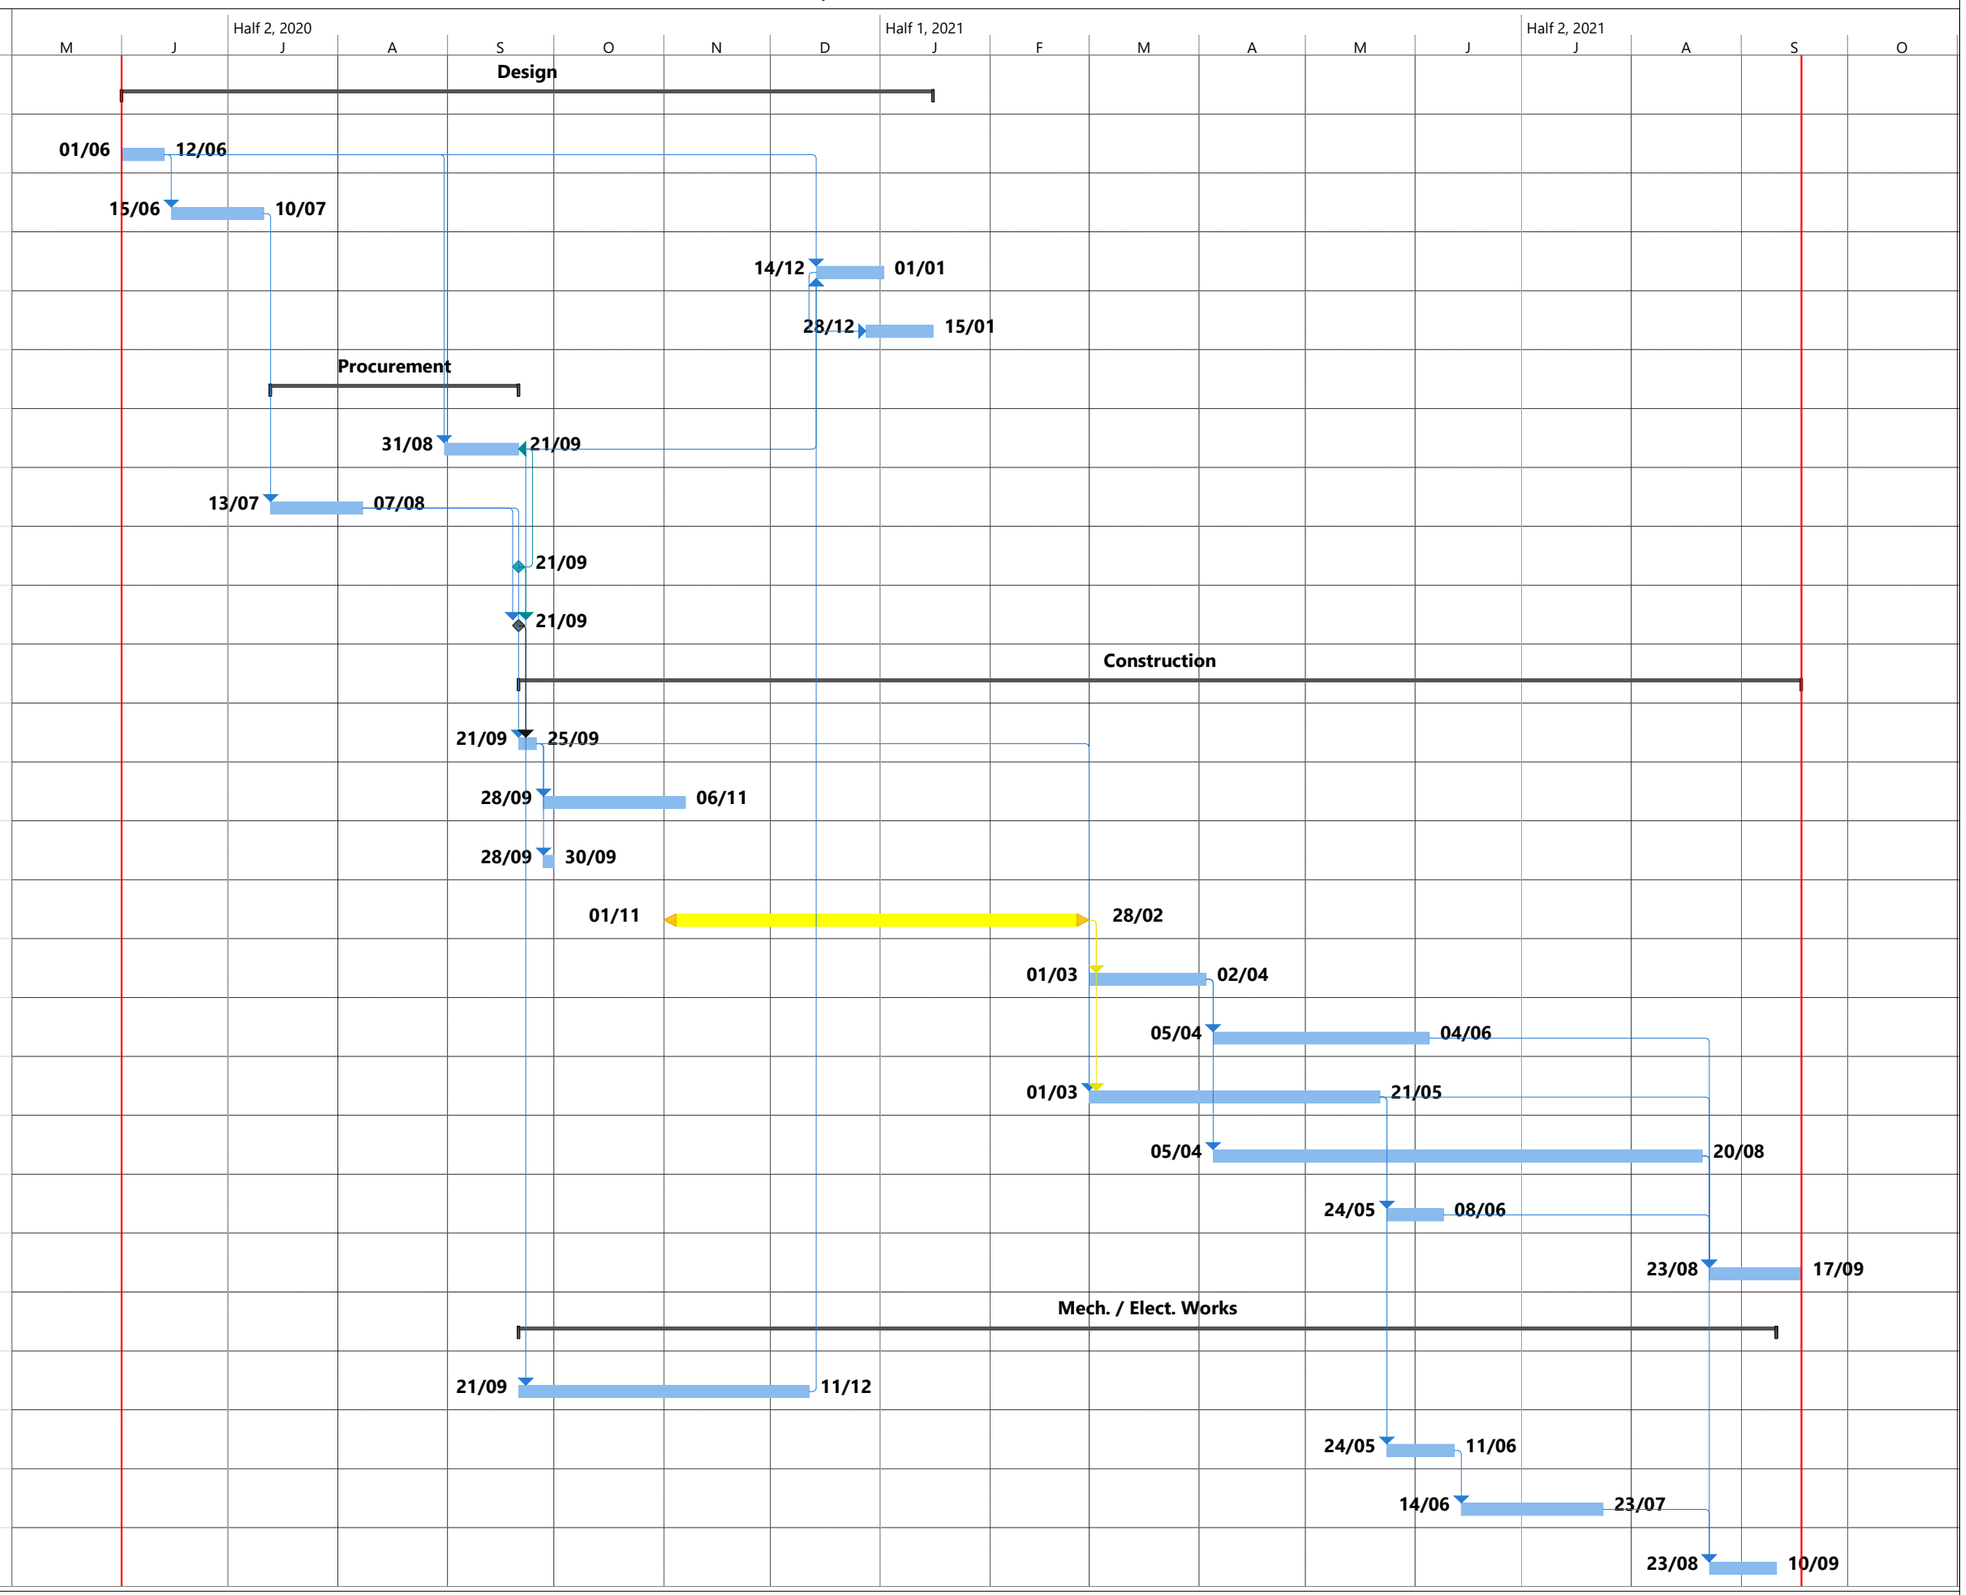ID	Task Name	Duration
1	**Design**	**165 days**
2	Tender design	10 days
3	Civil works design	20 days
4	Powehouse design	15 days
5	Electrical design	15 days
6	**Procurement**	**50 days**
7	Turbine procurement	15 days
8	Civil works tender	20 days
9	Financial Close	0 days
10	Civil works contract signature	0 days
11	**Construction**	**260 days**
12	Topographic survey and set out	5 days
13	Tree felling	30 days
14	Site set up	3 days
15	**Winter Break**	**87 days**
16	Access tracks / laydown areas	25 days
17	Intake construction	45 days
18	Powehouse construction	60 days
19	Pipeline works	100 days
20	Tailrace construction	12 days
21	Reinstatement	20 days
22	**Mech. / Elect. Works**	**255 days**
23	Turbine specs lead time	60 days
24	Turbine installation	15 days
25	HV/LV works	30 days
26	Commissioning	15 days
